

QUARTERLY STATUS

<b>Overview:</b>	<b>Horizontal:</b>
- HSSE: 3 recordable incidents this quarter	- Design in-progress: campus IT, Bettie Cram Drive bridge (by DOTI), pedestrian bridge
- NWC Program schedule - SPI 1.00 *	- Procurement in-progress: campus IT
- NWC Program budget - CPI 1.00 *	- Construction in-progress: utilities, pond A-1, Riverfront Open Space art
	- Completed: Riverfront Open Space opened to public
<b>Program-Wide:</b>	
- Continued horizontal/vertical design, procurements	
- Continued regulatory planning and permitting	
- Continued Public Art process	<b>Vertical:</b>
- Continued Livestock Center construction	- Livestock Center: site utilities, grading, foundations and piers under construction; trade contractor bidding and procurement in progress *
	- Equestrian Center: by NWCA
* Continuing to assess potential COVID-19, market impacts, design options, costing, recovery opportunities on program / schedule	

Livestock Center Arena Bowl Construction




MAJOR CONTRACTS AND PROCUREMENT STATUS

	Vendor	Description	Contracted Date	Amount
Contracted	Wilson & Co	Brighton Blvd - Design	Dec 2016	\$ 1,050,044
	Moore Iacofano Goltsman (MIG)	Campus Placemaking	Jun 2017	\$ 5,000,000 *
	Saunders Construction LLC	Demolition and Abatement	Sep 2017	\$ 18,000,000 *
	Kiewit Infrastructure Co	Brighton Blvd - Construction	Dec 2017	\$ 12,604,322
	Merrick & Company	Horizontal Design	Apr 2018	\$ 25,000,000 *
	Wilson & Co	DRIR Rail Consolidation	Apr 2018	\$ 2,190,687
	Hensel Phelps Construction	Horizontal Integrated Construction (HIC)	Jun 2018	\$ 275,000,000 *
	Short, Elliot and Hendrickson (S.E.H.)	Maint. & Ops Facility - Design	Sep 2018	\$ 776,758
	HKS, Inc.	Stockyards Event Cntr / Stockyards - Design	Nov 2018	\$ 3,659,443
	G.H. Phipps	Maint. & Ops Facility - Precon	Dec 2018	\$ 15,000
	Adolfson & Peterson	Stockyard Event Cntr / Stockyards - Precon	Mar 2019	\$ 37,500
	Populous	Equestrian Center / Parking Garage - Design	May 2019	\$ 10,831,281
	G.H. Phipps	Maint. & Ops Facility - CM/GC	Dec 2019	\$ 5,335,422
	Adolfson & Peterson	Stockyard Event Cntr / Stockyards - CM/GC	Dec 2019	\$ 8,529,490
	Whiting - Turner	Equestrian Center / Parking Garage - Precon	Dec 2019	\$ 2,443,650
	Populous	Livestock Center - Design	Feb 2020	\$ 10,557,527
	Whiting - Turner	Livestock Center - Precon	Oct 2020	\$ 2,016,700
	Whiting - Turner	Livestock Center - CM/GC	Sep 2022	\$ 204,751,561
Future	Whiting - Turner	Equestrian Center / Parking Garage - CM/GC	TBD **	TBD

KEY PERFORMANCE INDICATORS

Description	Status
Health , Safety, Security, and Environment	Yellow
Cost	Yellow
Schedule	Green
Design	Green
Community	Green
ReNEWW	Green
Concurrent Operations	Green

FINANCIAL SUMMARY

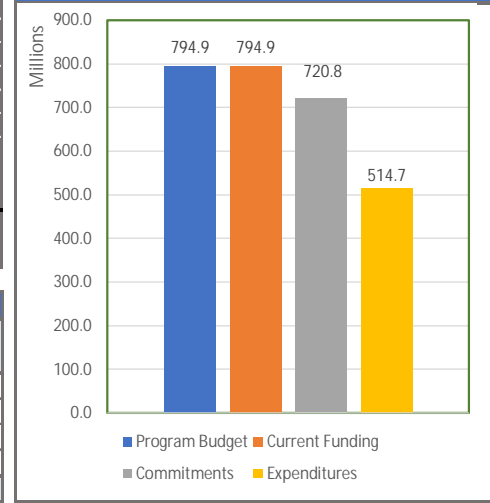

BUDGET, COMMITMENTS AND COST

PROGRESS/PERFORMANCE

Portfolio	Program To Date			Percent Complete	SPI
	Budget	Commitment	Cost		
Planning and Design Studies	4,793,446	4,793,445	4,793,445	100.0%	1.00
Horizontal	396,841,397	378,271,193	372,351,571	95.1%	1.00
Vertical	333,910,827	290,477,491	91,185,599	29.6%	1.00
Program Wide	59,304,540	47,270,778	46,331,369	76.7%	1.00
<b>Total Program</b>	<b>794,850,210</b>	<b>720,812,908</b>	<b>514,661,985</b>	<b>66.2%</b>	<b>1.00</b>

Commitment = Contracted obligations and expenditures

KEY SCHEDULE MILESTONES

Activity/ Milestone	Completion Date *
Program Substantial Completion	TBD
DRIR Rail Consolidation Complete	02/23/21 A
Delgany Interceptor Construction Complete	04/30/21 A
SYEC, Bison Pens and Plaza Substantial Completion	12/15/21 A
Stockyards Substantial Completion	12/31/21 A
Equestrian Center Substantial Completion	TBD
Livestock Center Substantial Completion	11/28/25
Pedestrian Bridge Substantial Completion	TBD
51st Ave Bridge Substantial Completion	09/02/22 A
Bettie Cram Drive Bridge Substantial Completion	TBD
CSU Animal Health Building Pad Ready	03/09/20 A
CSU Water Resources Center Pad Ready	09/14/20 A
CSU Center Pad Ready	09/14/20 A
WSSA Legacy Building Pad Ready	TBD

Riverfront Open Space and CSU Hydro Backyard Community Celebration - June 2023



Gray shading = Complete A = Actual Date  
 \* Continuing to assess potential COVID-19, market impacts, design options, costing, recovery opportunities on program/schedule
