




NWC CAC CONSTRUCTION UPDATE

April 2021


NWC CAMPUS PLAN


1. RTD Transit Station
2. Brighton Blvd. – 47th to Race Court
3. South Platte Riverfront
4. New National Western Drive
5. Stockyards Events Center
6. The Yards Multi-Use Space
7. Campus-related transit-oriented development (TOD)
8. New Bridges Near 48th & 51st Avenues
9. Livestock Center
10. Equestrian Center
11. District energy system's central utility plant (CUP)
12. CSU System Spur: Vida (health)
13. CSU System Spur: Hydro (water)
14. CSU System Spur: Terra (food)
15. Maintenance & Operations Facility
16. DRIR Rail Corridor
17. WSSA Legacy Building HQ
18. Pedestrian Bridge
19. Arena
20. Expo Hall
21. 1909 Rehabilitation
22. Supporting Development

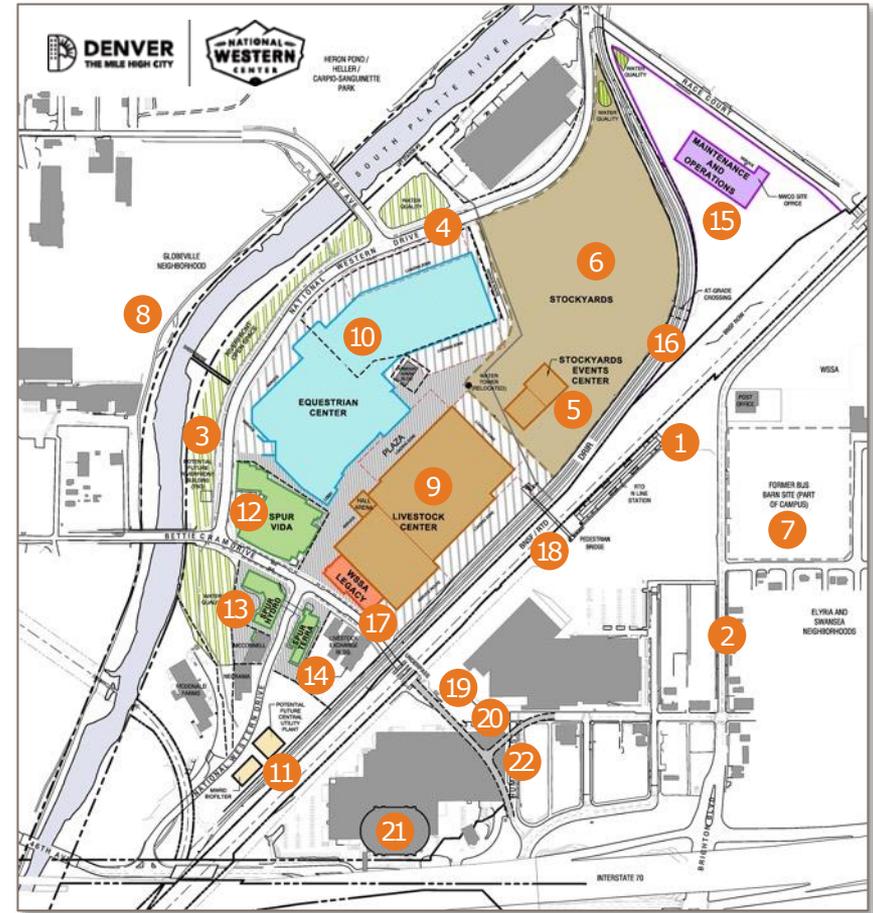

CONSTRUCTION AT A GLANCE

Aerial Photograph Dated
April 2, 2021

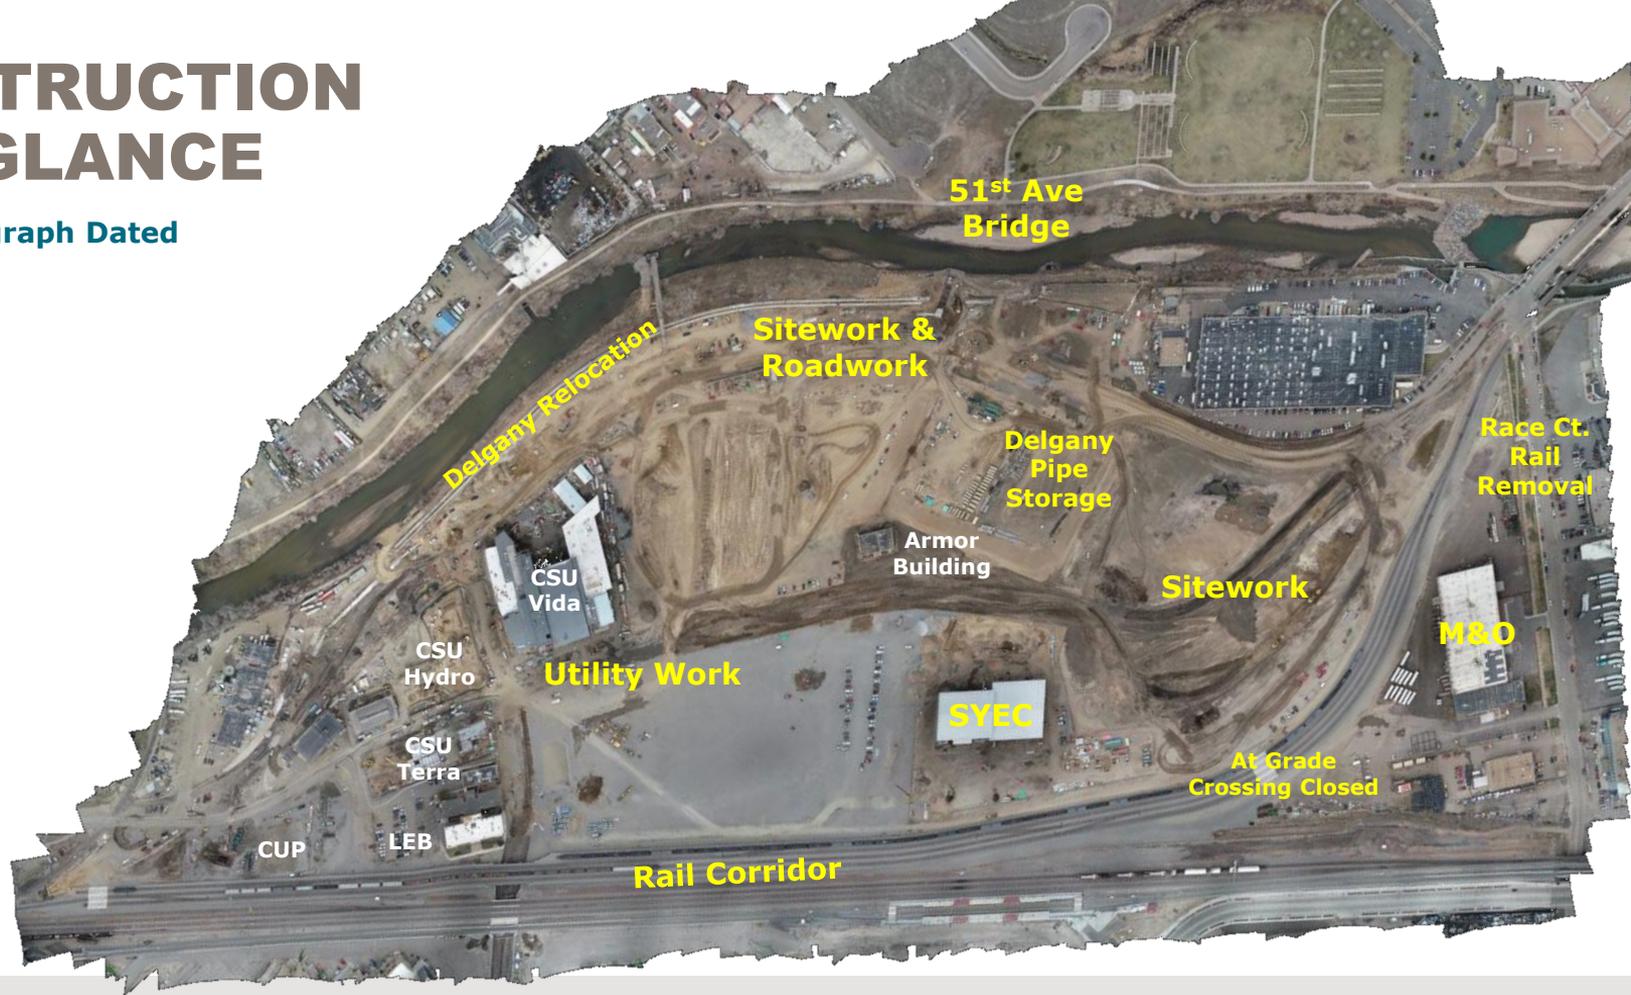

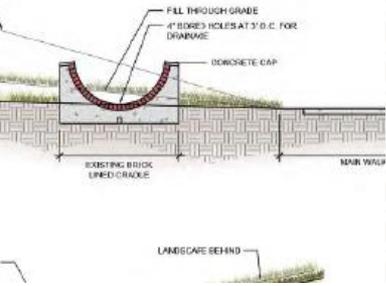

Construction continues on the new National Western Drive. About 90% of the new Delgany pipes have been installed, with the remainder being stored on-site. In this aerial view, you can see a new siphon structure, which will eventually be buried underground.



These photos show close up views of the new Delgany system and the new siphon structure.






The majority of the utilities are complete within this section of Bettie Cram, but a few final connections are underway seen here with the large trench. Preparations are underway for paving.



 **DENVER**
THE MILE HIGH CITY



Work continues on the exterior of the Stockyards Event Center (SYEC). All exterior staircases are complete and the main entry door installation will take place in the next several weeks. Grading continues on the East side of the building in preparation for additional work on the bison pens and loading areas.

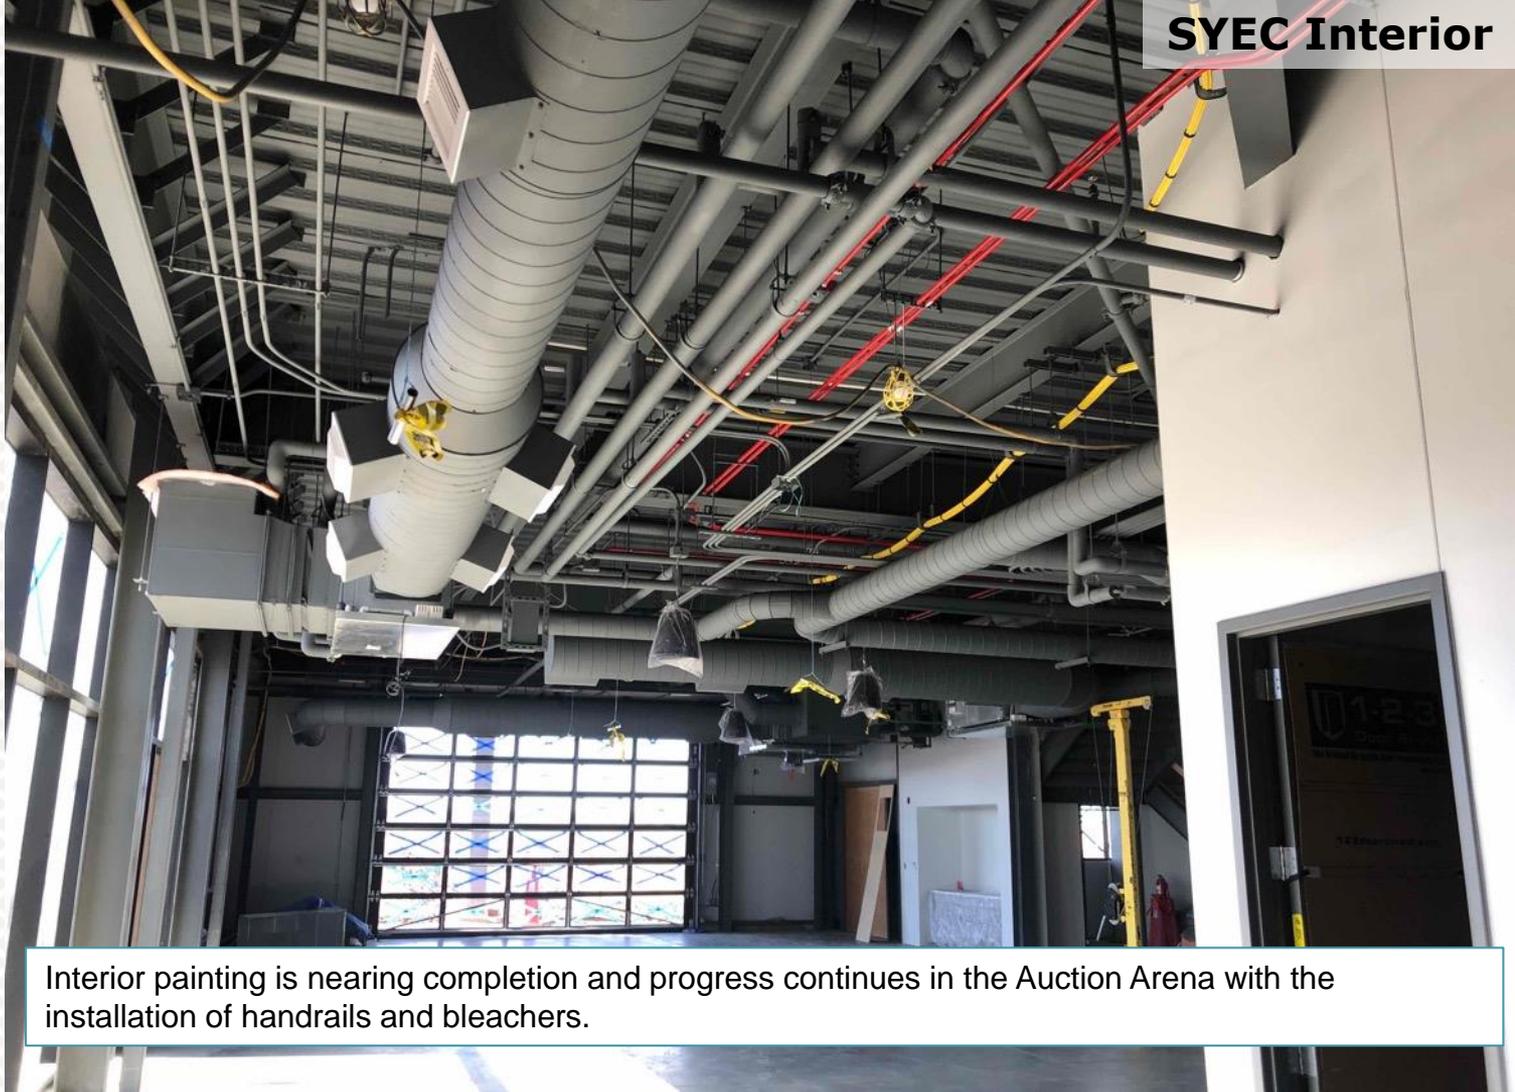


Interior painting is nearing completion and progress continues in the Auction Arena with the installation of handrails and bleachers.

View from west side of river, north of the 51st Ave. Bridge



CONSTRUCTION UPDATE:

- Active construction – August 2021
- Trail Detour – August/ September 2021
- Bridge preparations (piers & girders) – Q4 2021
- Abutment – Q1 2022
- Bridge landing & art installation – Q2 2022
- Roadway paving and sidewalks – Q3 2022

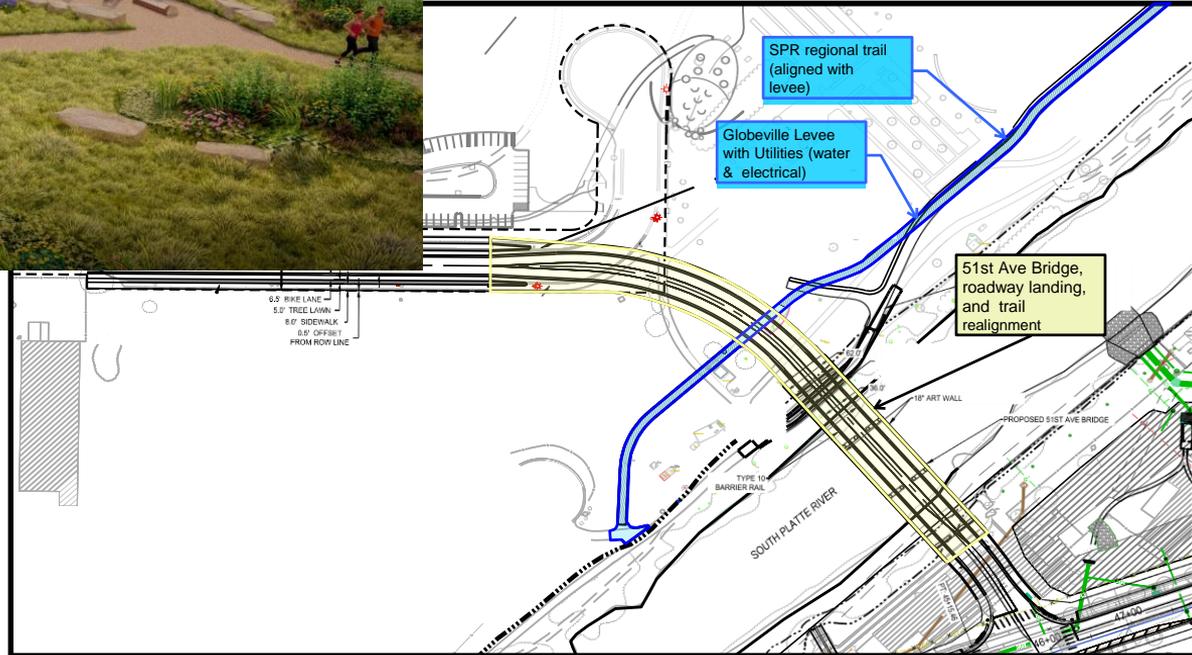

51ST Ave Bridge / Heron Pond Coordination



THANK YOU!

